


PREPARED BY  
HIGHWAY PLANNING SURVEY  
IN COOPERATION WITH  
U. S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA  
DEPARTMENT OF HIGHWAYS  
ROAD LIFE STUDIES  
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 1402  
TRUNK HIGHWAY 32  
COUNTY Clay  
DISTRICT 4A

LIMITS: Jct. T.H. 34 - Jct. T.H. 10



YEAR BUILT	PROJECT N <sup>o</sup>	DESCRIPTION			CODE N <sup>o</sup>
		TYPE	WIDTH	THICKNESS	
		Gravel	20'	1 1/2"	No Record of Constr. Added in 1934.
1921		Grading Gravel	22' 20'	2 1/2"	Co. Job N <sup>o</sup> 2101. 1000 C.Y./Mile. Added in 1934.
1923		Grading Gravel	24' 20'	1"	Co. Job N <sup>o</sup> 2301. Added in 1934.
1924		Grading Gravel	22' 20'	2 1/2"	Co. Job N <sup>o</sup> 2402. 1000 C.Y./Mile. Added in 1934.
1934	32-177-22	Grading	30'		
1935	32-177-22	Gravel	20'	2 1/2"	1000 C.Y./Mile.
M	1942 A.F.E. 6	Spot Graveling			131 C.Y./Mile. Maint. Dept.
M	1947 A.F.E. 6	Grav. Resurfacing			4203 Tons
C	1947 1402-02	Grading & Stab. Gravel	36' 28'	2"	1200 C.Y./Mi.
C	1951 1402-03	Grading Gravel Ext. #46 Cully.	32' 28'	2"	(6'-9" Grav. Fill placed from Mi. Pt. 5.53-5.92) Spot Grav. Subgr. Treat.
C	1951 A.F.E. 16	Bit. Surfacing Mixed Bit. (Mixed Prime)	32'	1 1/2"	MG2, 8047 Gal. Agg. 340 C.Y.
C	1952 1402-05 (1)	Grading Gravel	32' 28'	1 1/2"	700 C.Y./Mi.
C	1952 1402-06	Gravel Base Mixed Bit.	28' 26'	1 1/2"	Exc. from Mi. Pt. 5.48-5.87 which has base in p)
M	1954 A.F.E. 605	Light Bit. Seal	24'		RS2 & MG2, 19474 Gal. Agg. 685 C.Y.

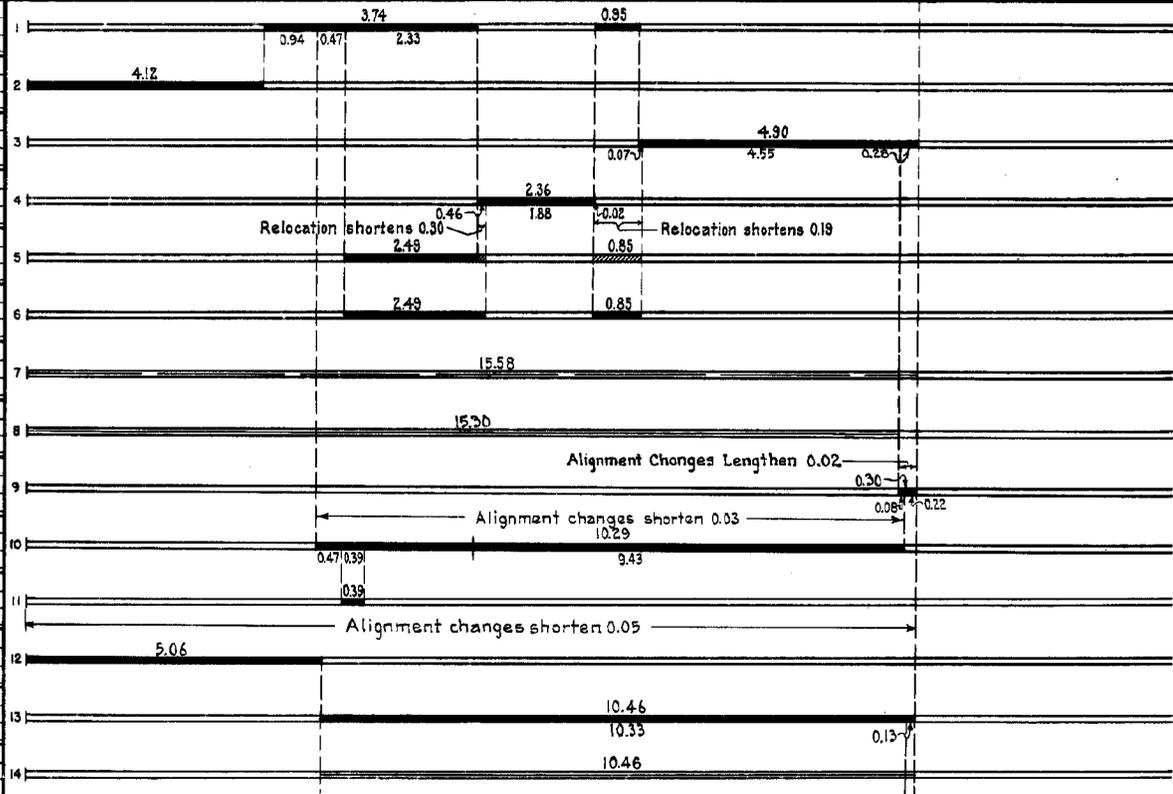

YEARS FROM	TOTAL MILES TO	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
		RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1934	1934	16.07	0.00	0.00	0.00	16.07	0.00	0.00	0.00
1934	1946	15.58	0.00	0.00	0.00	15.58	0.00	0.00	0.00
1947	1950	15.60	0.00	0.00	0.00	15.60	0.00	0.00	0.00
1951	1951	15.57	0.00	0.00	0.00	15.57	0.00	0.00	0.00
1952	1952	15.52	0.00	0.00	0.00	15.52	0.00	0.00	0.00
1957	1957	15.50	0.00	0.00	0.00	15.50	0.00	0.00	0.00

REMARKS: Layout is to scale as of 1934  
 (1) Contract not final but work substantially complete.



