


PREPARED BY  
HIGHWAY PLANNING SURVEY  
IN COOPERATION WITH  
U. S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA  
DEPARTMENT OF HIGHWAYS  
ROAD LIFE STUDIES  
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 3408  
TRUNK HIGHWAY 23  
COUNTY Kandiyohi  
DISTRICT 8A

LIMITS: Jct. T.H. 9 - E. Co. Line.



YEAR BUILT	PROJECT N <sup>o</sup>	DESCRIPTION			CODE N <sup>o</sup>
		TYPE	WIDTH	THICKNESS	
		Gravel	22'	2"	No Record of Constr.
		Earth	22'		No Record of Constr.
1925		Gravel	22'	2 1/4"	900 C.Y. / Mile. Maint. Dept.
1932	23-4-44-2	Grading	40'		
	(1)				
1932	23-4-44-2	Oil Tr. Gravel	22'	1 1/2"	25893 Gal. / Mile. Maint. Dept.
M	1940 A.F.E. 34	Bit. Seal Coat (High Type)			RT-9, 3440 Gal. / Mi. Grav. 100 C.Y. / Mi. Maint. Dept.
M	1944 A.F.E. 5	Bit. Seal Coat			Bit. 2814 Gal. / Mi. Agg. 115 C.Y. / Mi. Maint. Div.
M	1947 A.F.E. 5	Bit. Seal Coat			RC-3, 29838 Gal. Agg. 960 C.Y.
C	1955 3413-02	Grading	40'		
	3413-03	Bit. Stab. Base Plant Mix Bit.	40'	6"	On 12" Sand-Gr. & Salv. Mat'l Sub-base
C	1956 3408-02	Grading	40'		
		Bit. Stab. Base Plant Mix Bit.	40'	6"	on 0" 12" Granular Mat'l or Sand-Grav. Sub-base
M	1958 A.F.E. 605	Bit. Seal Coat	25'		RC-5, 28287 Gal. Agg. 980 C.Y.
C	1971 3408-09	Grading & Base Plant Mix Bit. Bit. Shoulders	24'		Channelization Rt. & Lt.
M	1977 SF	Bit. SHOULDERS & RIGHT TURN LANES	10'	3"	BA-1 188+ Ton
M	1977 SF	Bit. SHOULDERS	10'	3"	AC-1 795 Ton

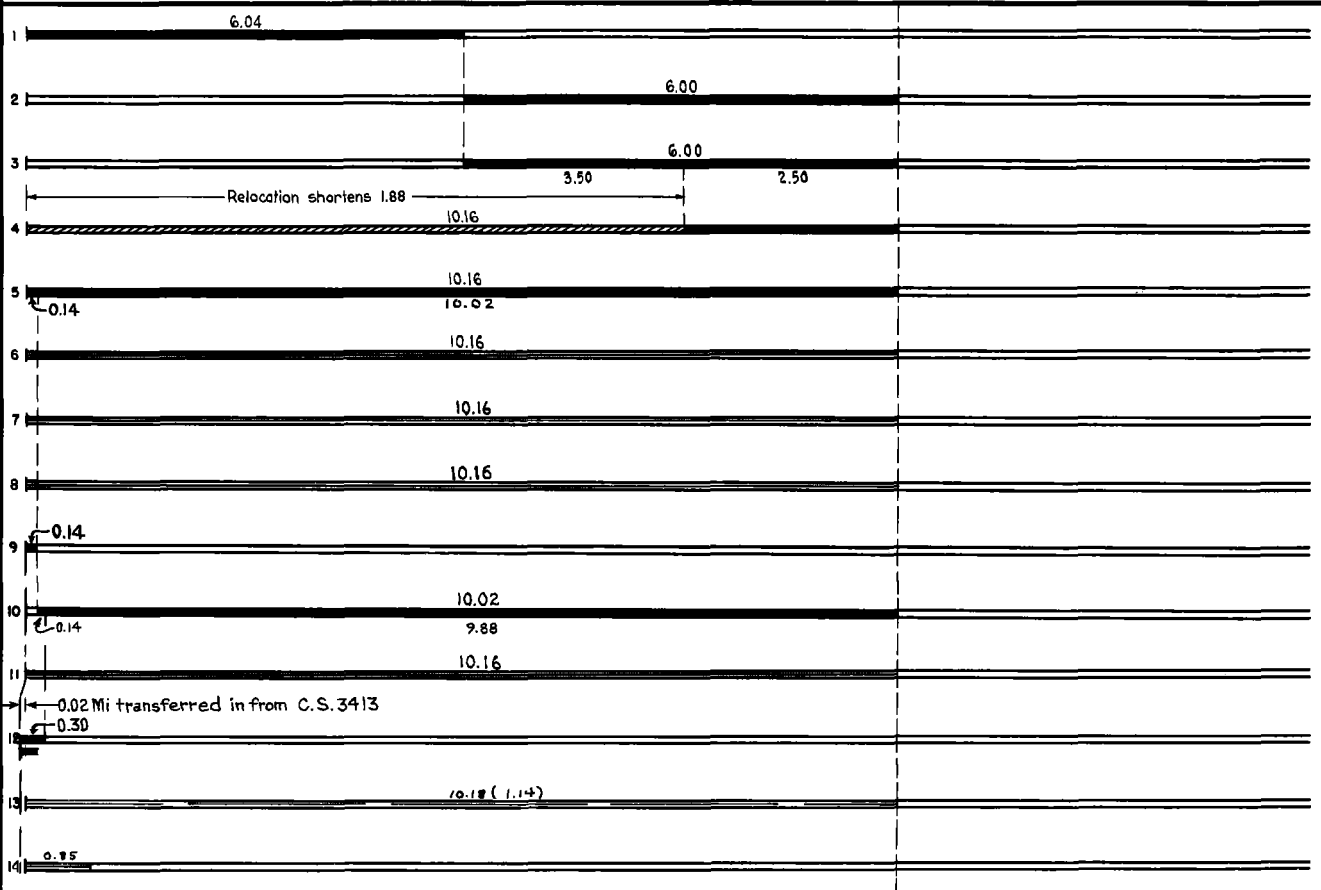

YEARS FROM	TOTAL MILES TO	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
		RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1921	1931	12.04	0.00	0.94	0.00	12.04	0.00	0.00	0.00
1932	1970	10.16	0.00	0.00	0.00	10.16	0.00	0.00	0.00
1971		10.18	0.00	0.00	0.00	10.18	0.00	0.00	0.00

REMARKS: Layout is to scale as of 1932.

(1) This work not done under this project number but lies within the limits of this project.

