


PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U.S. PUBLIC ROADS ADMINISTRATION

STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 3416
TRUNK HIGHWAY 104
COUNTY Kandiyohi
DISTRICT 4B

LIMITS: YY. Jct. T.H. 9 - N. Co. Line.

Ref. Pt. 014+00.446 - 018+00.435

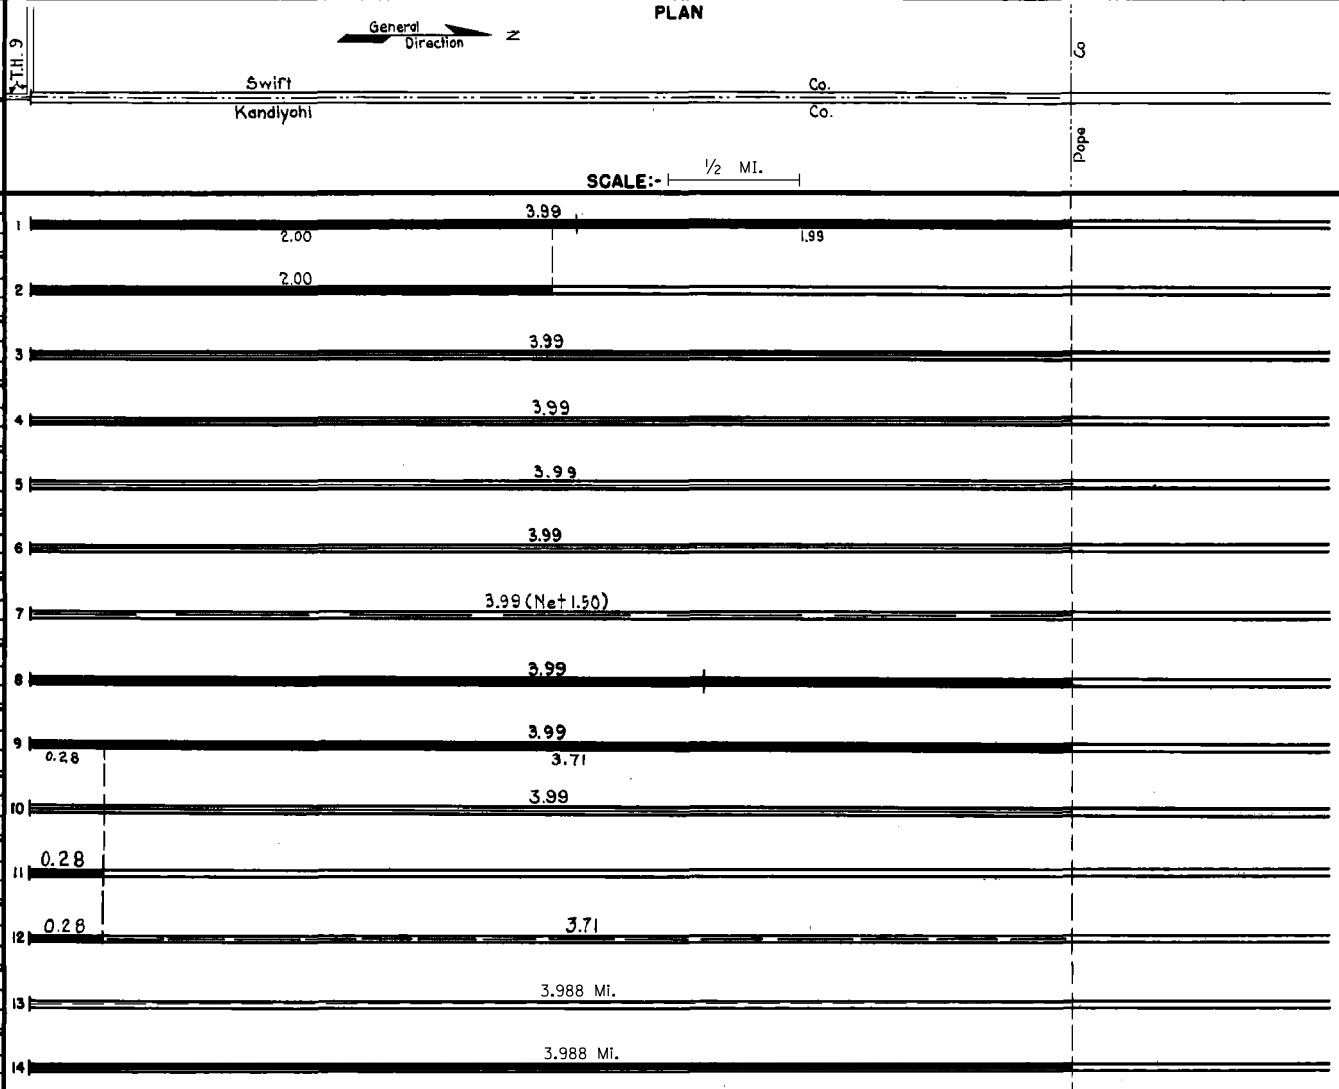

YEAR BUILT	PROJECT N°	DESCRIPTION			CODE N°
		TYPE	WIDTH	THICKNESS	
					No Record of Constr.
		Gravel	22'	1 1/2"	Added in 1934.
		Br. 3920	19'		12 Conc. Arch.
1935	104-143-21	Gravel	22'	1 1/2"	500 C.Y. / Mile. Relief Labor.
M					
1940	A.F.E. 12	Regravelling			329 C.Y./Mile. Maint. Dept.
M					
1943	A.F.E. 6	Grav. Resurface			313 C.Y./Mi. Maint. Dept.
M					
1946	A.F.E. 6	Grav. Resurfacing	20'		1612 C.Y.
M					
1951	A.F.E. 6	Grav. Resurfacing			1449 C.Y.
M					
1952	A.F.E. 6	Grav. Resurfacing (Spots)			573 C.Y.
C					
1954	3416-02	Grading Gravel Const. C108 Culy.	34' 26'	1 1/2"	700 C.Y./Mi.
C					
1955	3416-03	Stab. Sand-Gr. Subbase Stab. Grav. Base Plant Mix Bit.	30' 30' 24'	6" 3" 1 1/2"	
M					
1956	A.F.E. 605	Bit. Seal Coat	24'		RC-5, 12977 Gal. Agg. 438 C.Y.
C					
1959	3416-04	Grading Gravel Mix Bit. (Base)	42' 34' 26'	4" 1 1/2"	4666 Gal.
C&M					
1963	7606-16	Light Bit. Seal Plant Mix Bit Gravel Shoulders	25' 24'	2"	RS-2K, 7581 Gal. Seal Agg. 230 C.Y.
M					
1985	SF	Spot Overlay			
C					
1990	M4381	Bit. Overlay	24'	1 1/2"	Spec. 2341

YEARS		TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
FROM	TO		RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1934		3.99	3.99	0.00	0.00	0.00	0.00	3.99	0.00	0.00

REMARKS: Layout is to scale as of 1934.

