


PREPARED BY  
HIGHWAY PLANNING SURVEY  
IN COOPERATION WITH  
U.S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA  
DEPARTMENT OF HIGHWAYS  
ROAD LIFE STUDIES  
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 4607  
TRUNK HIGHWAY 16  
COUNTY Martin  
DISTRICT 7B

LIMITS: Jct. T.H. 15 in Fairmont - E. Co. Line



YEAR BUILT	PROJECT N <sup>o</sup>	DESCRIPTION			CODE N <sup>o</sup>
		TYPE	WIDTH	THICKNESS	
1921	16-9-22	Grading Br. 3577	30'	22"	
1922	16-9-22	Gravel	24'	3 1/2"	1600 C.Y./Mile
1932	16-9-22A	Grading Gravel Br. 5171	40'	30"	1 1/2" 40' B.S.
1934	16-9-22A	Concrete	20'	9-79	
1935	16-9-22D	Concrete	20'	9-79	
1936	16-9-22E	Concrete	20'	9-79	
C	1947	P.C. Concrete Widening	Var.	7 1/2"	
C	1955	Base* Plant Mix Bit.	56'	3"	*Conc. Imp. (except existing 56') widened to 56' with 7" conc.
C	1968	Pl. Mix. Bit. Surf.	56'	2"	Bit. Matl. 53 Ton
M	1970	SF Seal Coat	20'		CRS-2, 15556 Gal. Agg. 814 Tons
C	1971	Pl. Mix. Bit. Surf.	20'	2 1/2"	
M	1972	SF Seal Coat	20'		CRS-2, 14039 Gal. Agg. 729 Ton
C	1975	Bit. Overlay & Agg. Shoulders	20'	2 1/2"	AC Bit. 5657 Ton Agg. Cl. 6371 Ton
C	1976	Bit. Overlay	20'	2 1/2"	

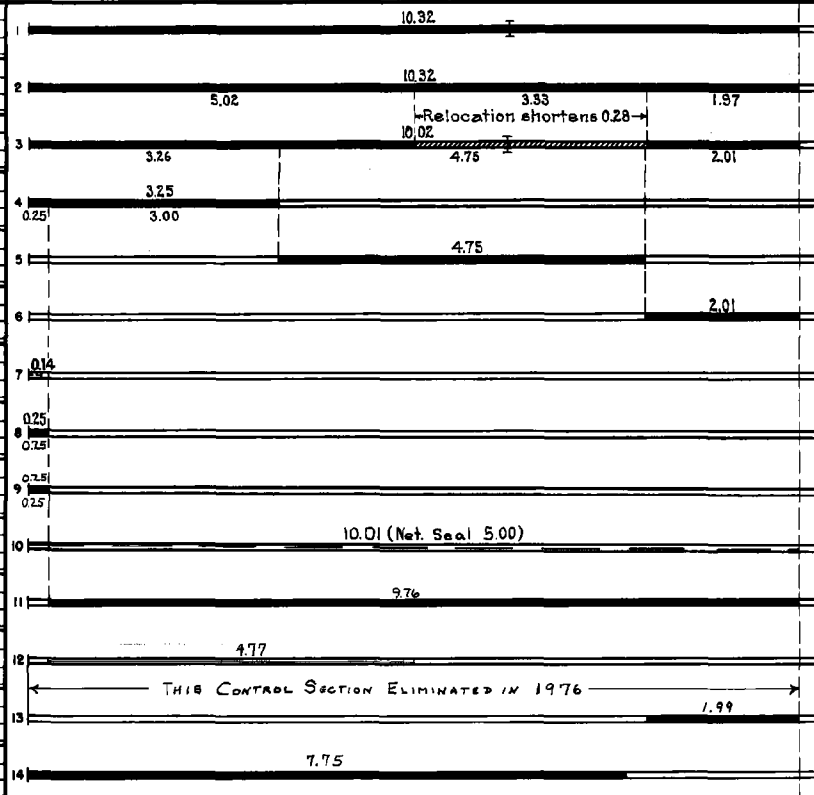

YEARS		TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN		REMARKS: Layout is to scale as of 1932
FROM	TO		RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	
1921	1931	10.32	10.07	0.01	0.24	0.00	10.07	0.01	0.24	0.00	
1932	1964	10.01	9.75	0.01	0.25	0.00	9.75	0.01	0.25	0.00	
1965		10.01	8.01	0.01	1.99	0.00	8.01	0.01	1.99	0.00	
