


PREPARED BY  
HIGHWAY PLANNING SURVEY  
IN COOPERATION WITH  
U. S. PUBLIC ROADS ADMINISTRATION

STATE OF MINNESOTA  
DEPARTMENT OF HIGHWAYS  
ROAD LIFE STUDIES  
CONSTRUCTION PROJECT LOG RECORD


CONTROL SECTION 4907  
TRUNK HIGHWAY 28  
COUNTY Morrison  
DISTRICT 3A

LIMITS: W. Co. Line (W. Corp. Limits of Swanville)- Jct. T.H. 27

Ref. Pt. 126+00.069 - 130+00.513



YEAR BUILT	PROJECT N <sup>o</sup>	DESCRIPTION			CODE N <sup>o</sup>
		TYPE	WIDTH	THICKNESS	
		Earth	24'		No Record of Constr.
1928	28-28-29	Grading Gravel Br. 4715 & 6078	32' 24' 27'	2 1/2"	1200 C.Y./Mile. 52' C.D.G. & W106D.
1930	(1) 28-28-29	Oil Tr. Gravel	30'	1"	13276 Gal./Mile. Maint. Dept.
1931	(1) 28-28-29	Oil Tr. Gravel	24'	2"	6570 Gal./Mile. Maint. Dept.
1937	A.F.E. 14 A.F.E. 2B	Subgrade Lift. Mixed Bit. Surface.	28' 24'	1 1/4"	Maint. Dept.
M	1941	A.F.E. 14 Bit. Retreat.	24'		SC3,6788 Gal./Mi. Grav. 363 C.Y./Mi. Maint. Dept.
M	1946	A.F.E. 4 Spot Treat. Bit. Surf. Repair	24'		SC3,17030 Gal. Agg. 1014 C.Y.
M	1948	A.F.E. 4 Spot Treat. Bit. Surf. Repair	24'		SC3,2M3,7747 Gal. Agg. 426 C.Y.
C	1952	A.F.E. 4 Bit. Resurfacing Mixed Bit.	24'	1" Added	SC-3,37184 Gal. Agg. 3143 Tons
M	1961	Light Bit. Seal	25'		RS-2,8827 Gal. Agg. 330 C.Y.
C	1971	4907-02 Pl. Mix Bit. Surf.	24'	2 1/2"	
C	1985	4907-03 Bit. Surfacing	28' 24'	1 1/2" 1"	Sp. 2341 Sp. 2331
M	2002	8823-32 Bit. Overlay	24'	1 1/2"	Spec. 2350
M	2008	8823-117 Bit. Seal Coat	24'		FA-2

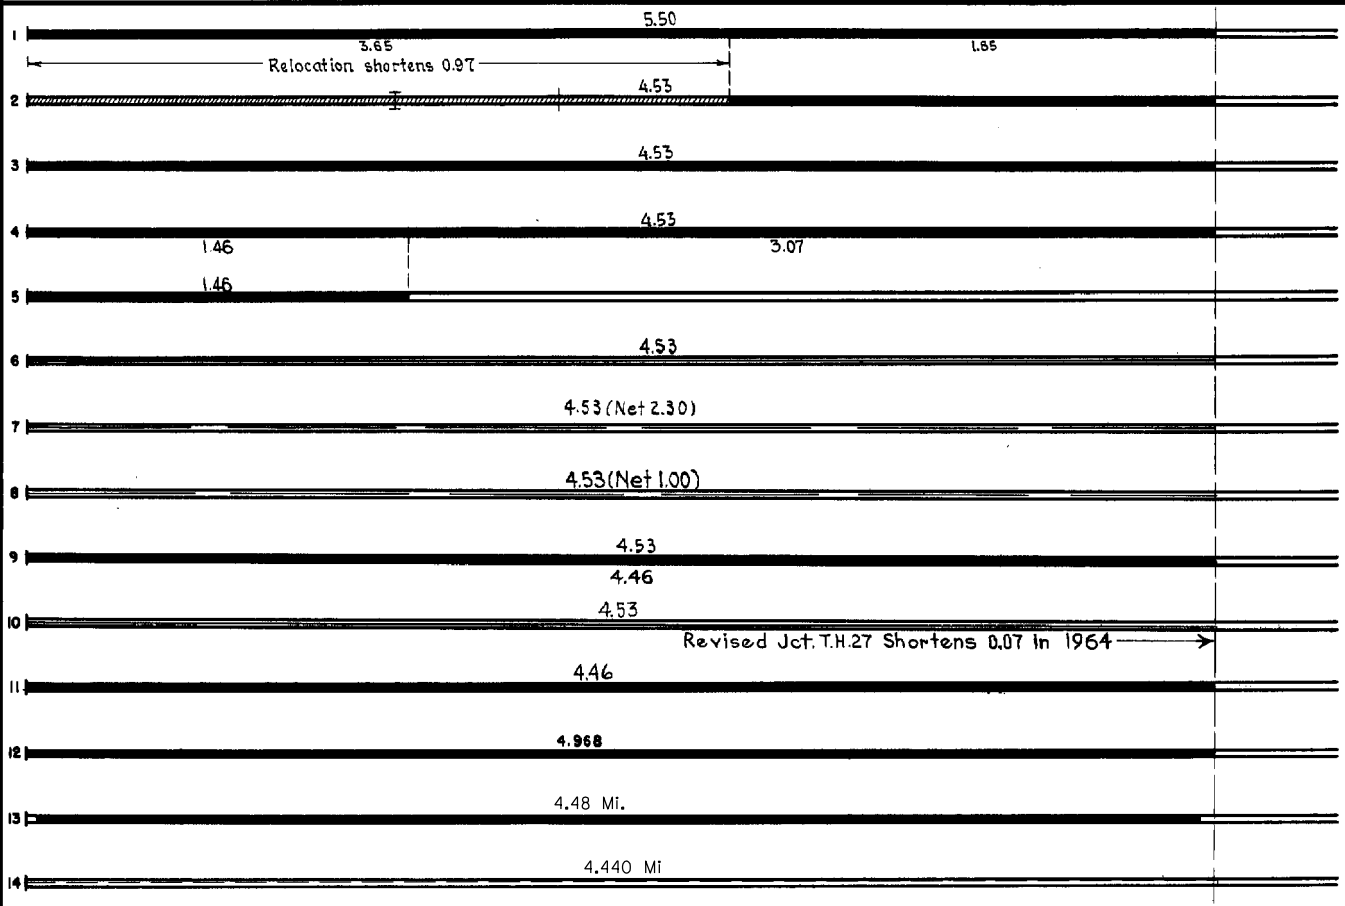

YEARS		TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN		REMARKS: Layout is to scale as of 1928.
FROM	TO		RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	
1921	1927	5.50	4.76	0.00	0.74	0.00	5.50	0.00	0.00	0.00	
1928	1963	4.53	4.45	0.01	0.07	0.00	4.52	0.01	0.00	0.00	
1964		4.46	4.38	0.01	0.07	0.00	4.45	0.01	0.00	0.00	(1) This work not done under this project number but lies within the limits of this project.

