R.L.-7 REV. 2-40

SHEET 1 OF 1

PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U. S. PUBLIC ROADS ADMINISTRATION

STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 6617
TRUNK HIGHWAY 21
COUNTY Rice
DISTRICT 6B

LIMITS: In Faribault from S. Jct. T.H. 35 - Jct. T.H. 3



YEAR BUILT	PROJECT Nº	DESCRIPTION TYPE	WIDTH	THICKNESS	REMARKS	CODE Nº
					Transferred from	
1932		Oil Tr. Gravel	26'		C.S. 6605 (21-21) in	
					1953.	
					Transferred from	
1937	21-21-26-2A	Br. 5658 (B.S.-U.P.)	36'		C.S. 6605 (21-21) in	
1938	A.F.E. 28	Mixed Bit.	26'	1"	1953.	
C		Grading	42'			
1953	6617-01	Sand-Gravel	42'	12"		
		Gravel	42'	1"	1000 C.Y./Mi.	
C		Bit. Stab. Base	38'	6"		
1955 (1)	6617-02	Plant Mix Bit.	24'	3"		
M					CRS-2, 5095 Gal.	
1967	C	Light Bit. Seal	25'		FA-2 Agg. 147 C.Y.	

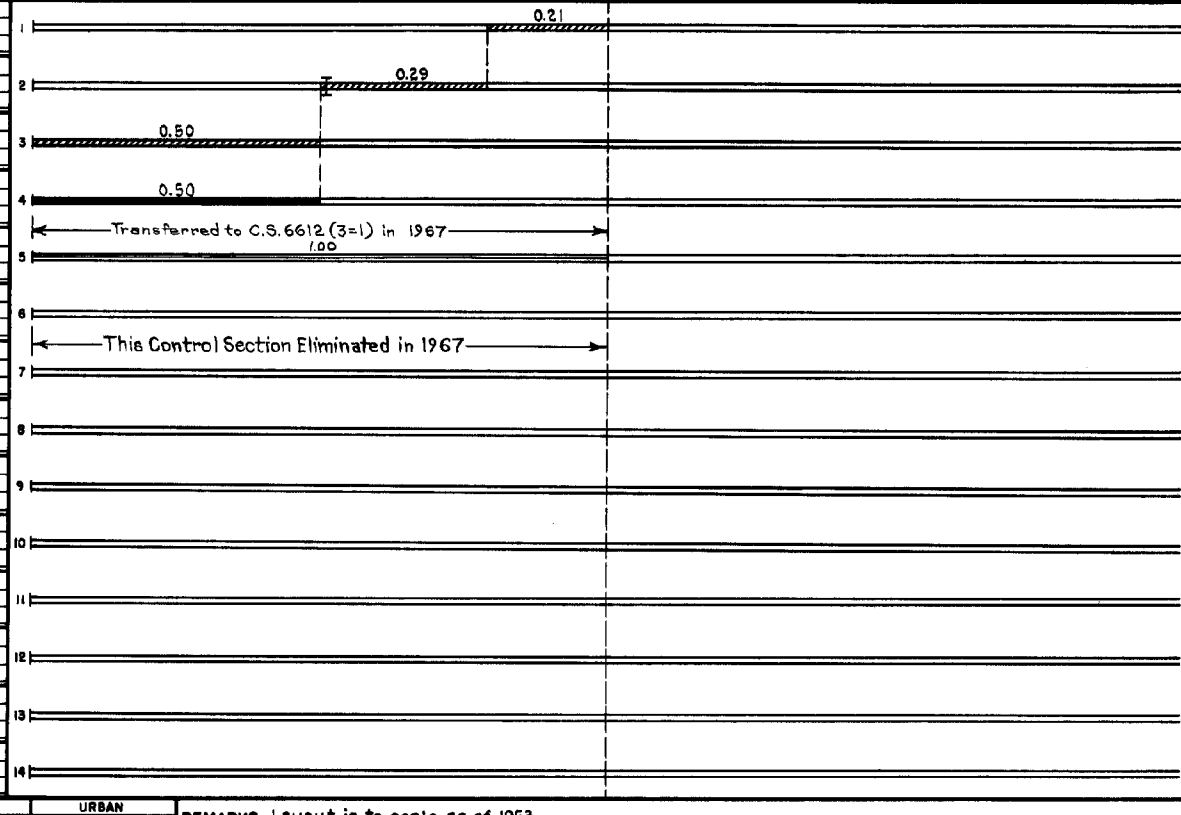

YEARS FROM	YEARS TO	TOTAL MILES	UNINCORPORATED RDWY. MI.	UNINCORPORATED BR. MI.	INCORPORATED RDWY. MI.	INCORPORATED BR. MI.	RURAL RDWY. MI.	RURAL BR. MI.	URBAN RDWY. MI.	URBAN BR. MI.
1953	1966	1.00	0.00	0.00	1.00	0.00	0.00	0.00	1.00	0.00
1967		0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00

REMARKS: Layout is to scale as of 1953
(1) Contract not final but work substantially complete.
