FORM R.L.-7 REV. 2-40

SHEET 1 OF 3

PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U. S. PUBLIC ROADS ADMINISTRATION

STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 3106
TRUNK HIGHWAY 6
COUNTY Itasca
DISTRICT 3A

LIMITS: W. Co. Line-Ejct. T.H.2 in Cohasset



YEAR BUILT	PROJECT Nº	DESCRIPTION: TYPE	WIDTH	THICKNESS	REMARKS	CODE Nº
		Gravel	27'	3"	No Record of Constr.	
		Br. 832 (1)	17'		195' B.S. & L.T.	
1920	6-34-2	Grading				
		Gravel	24'27'	2"-2½"	1000-1200 C.Y./Mile.	
		Grading	30'			
1923	6-34-24	Gravel	27'	2½"	1200 C.Y./Mile.	
		Br. 3252	19'		250' L.T. & Lift.	
		Grading	32'			
1935	6-34-26-2A	Br. 508			W108D	
		Br. 602			W108T	
1936	6-34-26-2A	$CaCl_2$ Stab. Grav.	32'	3"	With Clay	
		Stab. Grav. Base.	32'	3"	With Clay	
		Grading	24			
1937	A.F.E. 7	Gravel	24'	2¼"		
1939	3106-03	Mixed Bit. Surface	26'	1½"		
M 1943	3106-05	Base Repair & Bit. Surf. (Spots)	26'	1"		
M 1944	A.F.E. 6	Grav. Resurfacing	24'		278 C.Y./Mi. Maint. Div.	
M 1945	A.F.E. 4	Spot Treat. Bit. Surf. Repair	24'		MC-2, 5590 Gal./Mi. Grav. 265 C.Y./Mi. Maint. Div.	
C 1946	A.F.E. 21	Heavy Reshaping (2)	30'		SC-2 & 3, 109590 Gal.	
	A.F.E. 24	Gravel Lifts &	26'	3"-18"		
		Bit. Surf. Treat.	26'		(Mixed Prime)	
M 1947	A.F.E. 28	Bit. Surf. Repair	26'		SC-2&3, 37345 Gal.	
M 1948	A.F.E. 4	Spot Treat.			SC-3 & RC-1, 7736 Gal.	
		Bit. Surf. Repair	24'		Agg. 407 C.Y.	
		Spot Fog Seal	24'			
M 1950	A.F.E. 4	Spot Treat.			SC-3, 27410 Gal.	
		Bit. Surface Repair	24'		Agg. 1368 C.Y.	

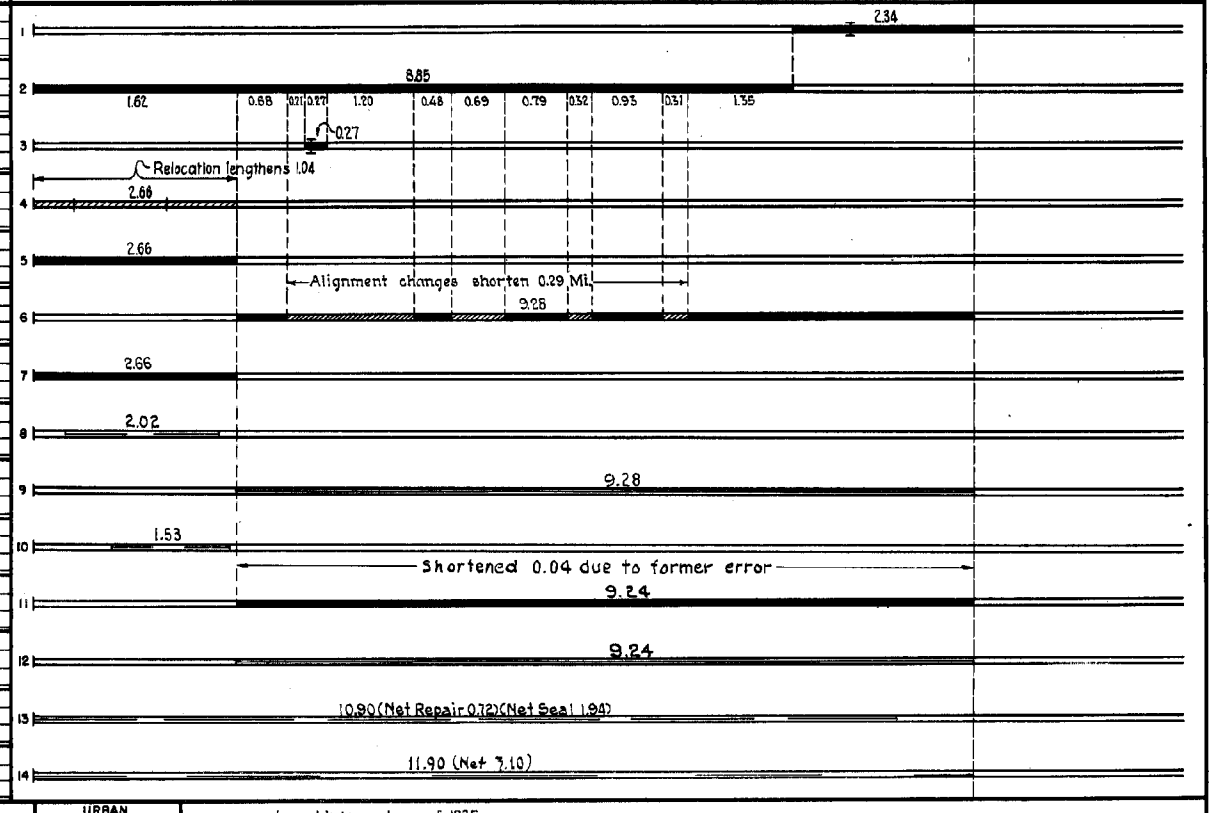

YEARS FROM	YEARS TO	TOTAL MILES	UNINCORPORATED RDWY. MI.	UNINCORPORATED BR. MI.	INCORPORATED RDWY. MI.	INCORPORATED BR. MI.	RURAL RDWY. MI.	RURAL BR. MI.	URBAN RDWY. MI.	URBAN BR. MI.
1921	1922	11.19	10.29	0.04	0.86	0.00	11.15	0.04	0.00	0.00
1923	1934	11.19	10.25	0.08	0.86	0.00	11.11	0.08	0.00	0.00
1935	1936	12.23	11.29	0.08	0.86	0.00	12.15	0.08	0.00	0.00
1937	1945	11.94	11.00	0.08	0.86	0.00	11.86	0.08	0.00	0.00
1946	1974	11.90	10.96	0.08	0.86	0.00	11.82	0.08	0.00	0.00
1975		11.90	11.82	0.08	—	—	11.82	0.08	—	—

REMARKS: Layout is to scale as of 1935.

(1) Br. 832 built in 1915. (2) Exception to reshaping Mi. Pts 3.46-4.96; 5.58-5.98; 6.89-7.06; 8.03-8.24; 11.72-11.90.

2-76

2-86

R.L.-7 REV. 2-40

SHEET 2 OF 3

PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U. S. PUBLIC ROADS ADMINISTRATION

STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 3106
TRUNK HIGHWAY 6
COUNTY Itasca
DISTRICT 3A

LIMITS: W. Co. Line - E. Jct. T.H. 2 in Cohasset

Ref. Pt. 067+00.451 - 077+00.726

YEAR BUILT	PROJECT Nº	DESCRIPTION: TYPE	WIDTH	THICKNESS	REMARKS	CODE Nº
M 1951	A.F.E. 4	Bit Fog Seal	24'		RCS-1, 15753 Gal. Agg. 380 C.Y.	
M 1952	A.F.E. 4	Spot Treat Bit. Surf. Repair	24'		SC-3, 550 Gal.	
C 1954	A.F.E. 821	Bit. Resurfacing Mixed Bit.	24'	1"	MC-3, 103737 Gal. Agg. 8333 Tons	
C 1957	3106-10	Grade X-ing Signals				
M 1958	A.F.E. 605	Light Bit. Seal	25'		RS-2, 21558 Gal. Agg. 1190 Tons	
M 1960		Spot Treat Bit. Surf. Repair	24'		MC-2, 2176 Gal. Agg. 168 Tons	
M 1964	C	Light Bit Seal	25'		RS-2K, 19147 Gal. Agg. 720 C.Y.	
C 1973	3106-11	Pl. Mix Bit. Resurf.	24'	1½"E 3"		
C 1978	3106-13	Grading	53'			
		Bit. Surf.	24'	3"		
	SF	Agg. Shoulders	10'	3"		
C 1984	3106-17	Grading, Base	36'	5"	Agg.	
		Bit. Surfacing	24'	3½"	2" Sp. 2331, 1½" Sp. 2341	
		Br. 31030			Repl. Br. 3252	
M 1985	SF	Wedge Paving		3"	Spec. 2331	
M 1985	SF	Bit. Shoulders	10'	1½"	Spec. 2331	
M 1985	SF	Wedge Paving		3"	Spec. 2331	
C 1988	3106-19	Bit. Overlay	28'	2" 1"	Spec. 2331 Spec. 2341	

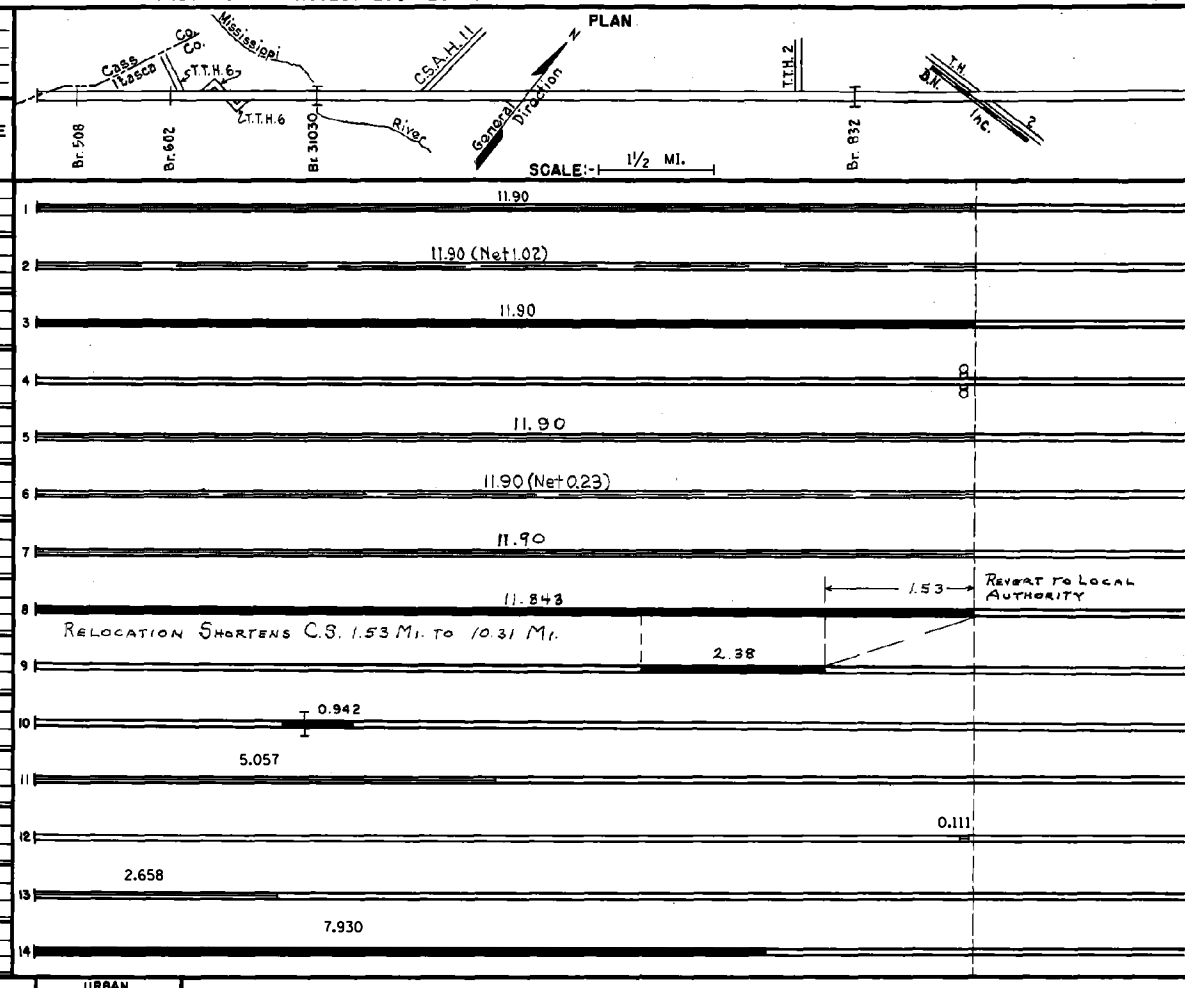

YEARS FROM	YEARS TO	TOTAL MILES	UNINCORPORATED ROWY. MI.	UNINCORPORATED BR. MI.	INCORPORATED ROWY. MI.	INCORPORATED BR. MI.	RURAL ROWY. MI.	RURAL BR. MI.	URBAN ROWY. MI.	URBAN BR. MI.

REMARKS: See Sheet No. 1

FORM RL-7

PREPARED BY
BUREAU OF POLICY & PLANNING
IN COOPERATION WITH
U. S. DEPARTMENT OF TRANSPORTATION - FEDERAL HIGHWAY ADMINISTRATION

STATE OF MINNESOTA
DEPARTMENT OF TRANSPORTATION
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 3106
TRUNK HIGHWAY 6
COUNTY ITASCA
DISTRICT 3A

LIMITS: CASS/ITASCA CO. LINE - E. JCT. USTH-2

REF. PT. 067-00.451 - 077-00.726



YEAR BUILT	PROJECT No	DESCRIPTION: TYPE	WIDTH	THICKNESS	REMARKS
M 1990	M4377	BIT. OVERLAY	VAR.	2"	SPEC. 2331
S 2002	3106-23	MILL & BIT. OVERLAY	28'	VAR.	SPEC 2350
		AGG. SHOULDER	VAR.	1.5"	CLASS 1
D 2006	D06055 8823-84	Bituminous Rout & Seal	24'		Spec. 3725
D 2007	8823-100	Agg. Seal			FA-2

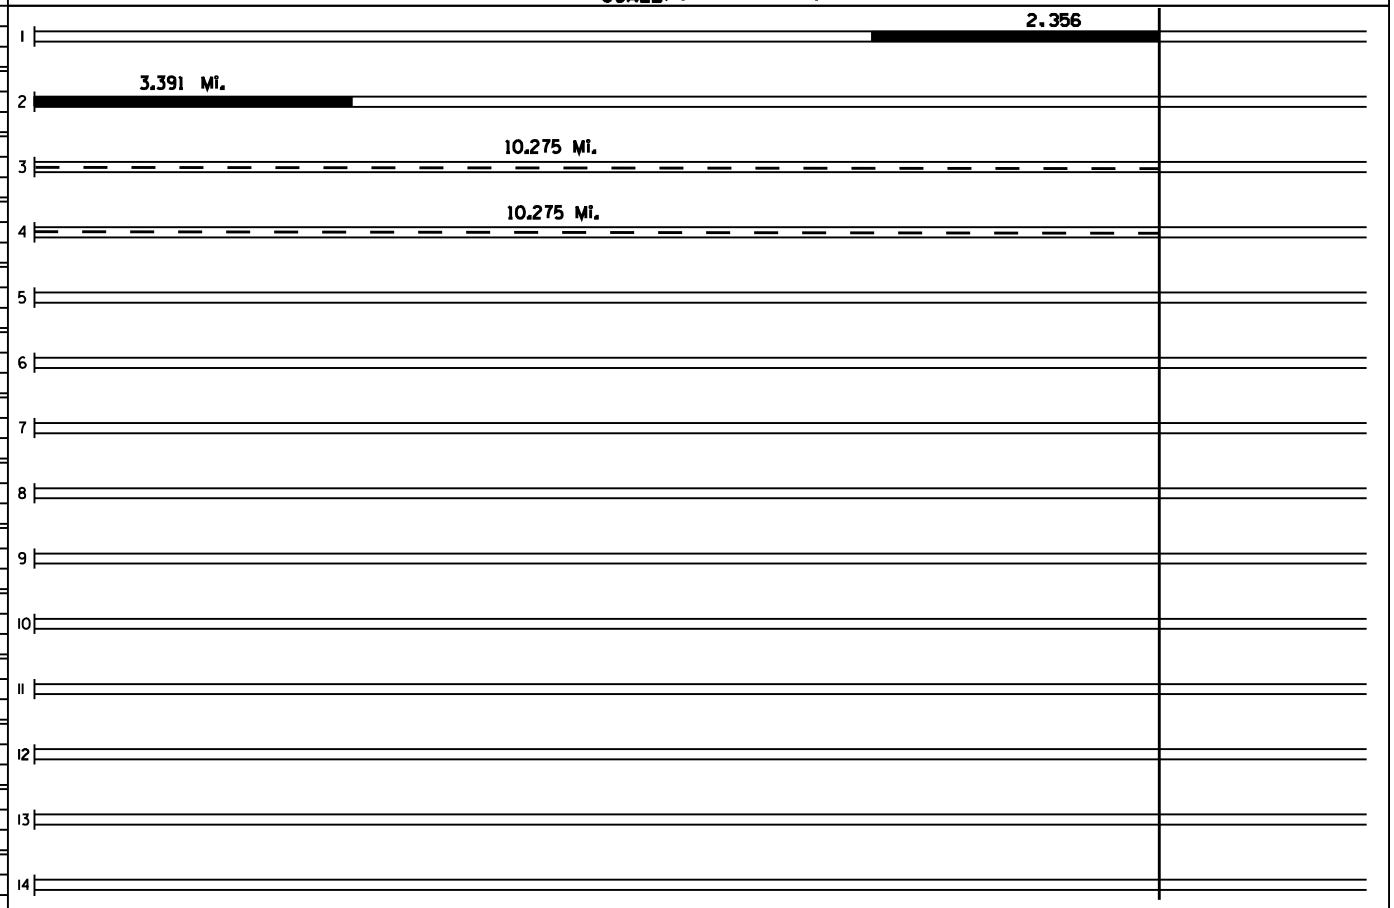

YEARS FROM	YEARS TO	TOTAL MILES	UNINCORPORATED RDWY. MI.	UNINCORPORATED BR. MI.	INCORPORATED RDWY. MI.	INCORPORATED BR. MI.	RURAL RDWY. MI.	RURAL BR. MI.	URBAN RDWY. MI.	URBAN BR. MI.

REMARKS:
